

Stage 3 construction starting September 17, 2018

Project Status& Update

September 13, 2018

COA, ST

Contractor finishing up stage 2 construction. Pavement markings and signage, along with Pace bus routes signs and boards, are being install. Starting Monday, September 17, 2018, the contractor will be switching from stage 2 to stage 3 construction. Stage 3 involves the construction of the new parking area (existing Pace staging area), installation of utilities (storm sewers, water hydrant, electrical conduits, parking lot lighting), construction of sidewalk, curb & gutter, and intersection improvements (removal of existing traffic signal and modification of existing entrance) on Broadway.

Commuters are reminded to pay special attention to permit & daily parking location signs, traffic controls/detour signs and avoid fenced-off work area. Commuters should continue to use the East Platform Parking Lot for ADA parking and for Drop off and Pick up. Pace riders should start using the new Pace bus staging area.

Businesses are open during construction. Access off of Broadway Avenue for Holiday Inn Express and Two Brothers Roundhouse are available and will remain open during this stage. Commuters and patrons of these businesses should follow the wayfinding signs for access to Spring Street and Broadway Avenue.

Commuters should note the temporary designated location of the daily fee and permit parking areas. Permit parking areas are available for daily fee users after 8 am. Temporary daily permit parking along Lincoln Avenue is available for commuters. .

Stage 3 work is anticipated to be completed in November 2018, weather permitting.


Contractor continue to monitor the water level of the Fox River, anticipating to start mobilization for drill shaft work.

Please contact the City Engineering Division at 630/256-3200, if you have any questions.

Construction Stage 3- Exhibit:

<https://www.aurora-il.org/DocumentCenter/View/4408/Construction-Stage-3->

Stage 2 Construction Pictures:

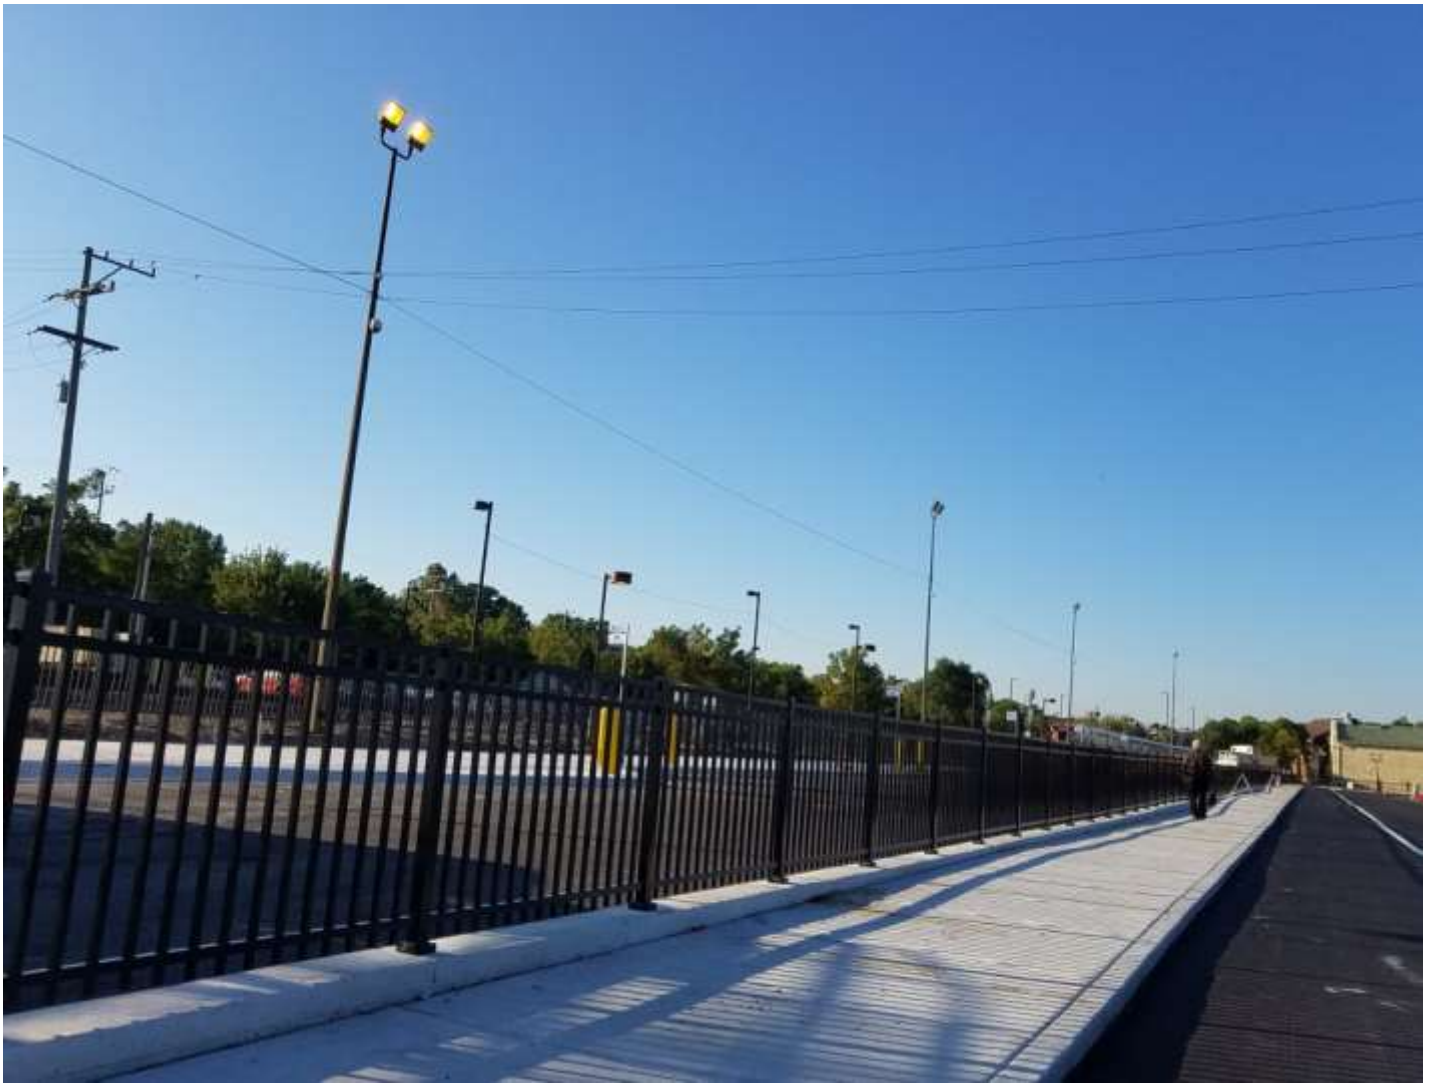

ATC Parking Lot- Installed fence along Kiss-n-Ride Area.



Stage 2- ATC Parking-Pace Staging Area- Installation of binder surface. Looking north



Stage 2. ATC Parking Lot- Installation of Binder Surface, looking west.
